# ALPINE CONSTRUCTION, LLC
## WAITSFIELD VILLAGE COVERED BRIDGE
## PROJECT SCHEDULE

| ID | Task Name |
|---|---|
| 1 | **COFFERDAM INSTALLATION** |
| 2 | EROSION PREVENTION & SEDIMENT CONTROL |
| 3 | COFFERDAM NORTH ABUTMENT |
| 4 | **BRIDGE ABUTMENT REPAIR** |
| 5 | BRIDGE SHORING SUPPPORT |
| 6 | DEMOLTION OF CONCRETE |
| 7 | NEW BRIDGE ABUTMENT |
| 8 | REMOVE SHORING SUPPORT |
| 9 | **PEDESTRIAN ABUTMENT CONSTRUCTION** |
| 10 | **SOUTH ABUTMENT CONCRETE** |
| 11 | STEM WALL - CONCRETE |
| 12 | **NORTH ABUTMENT CONCRETE** |
| 13 | CLASS C FILL POURS - 2 |
| 14 | FOOTING POURS -2 |
| 15 | STEM WALL |
| 16 | **BACKFILL STRUCTURES** |
| 17 | SOUTH ABUTMENT |
| 18 | NORTH ABUTMENT |
| 19 | **INSTALLATION OF NEW PEDESTRIAN BRIDGE** |
| 20 | DELIVERY OF BRIDGE |
| 21 | INSTALLATION OF BRIDGE |
| 22 | TIMBER, SIDING, & ROOF INTEGRATION |
| 23 | GREEN MOUNTAIN POWER - POLE INSTALLATION |
| 24 | **BRIDGE STREET RECONSTRUCTION** |
| 25 | SUB-BASE |
| 26 | INSTALL SIDEWALKS |
| 27 | INSTALL GUIDE RAILS |
| 28 | TRAFFIC SIGNS |
| 29 | BITUMINOUS PAVEMENT - BASE COURSE |
| 30 | BITUMINOUS PAVEMENT - TOP COURS |

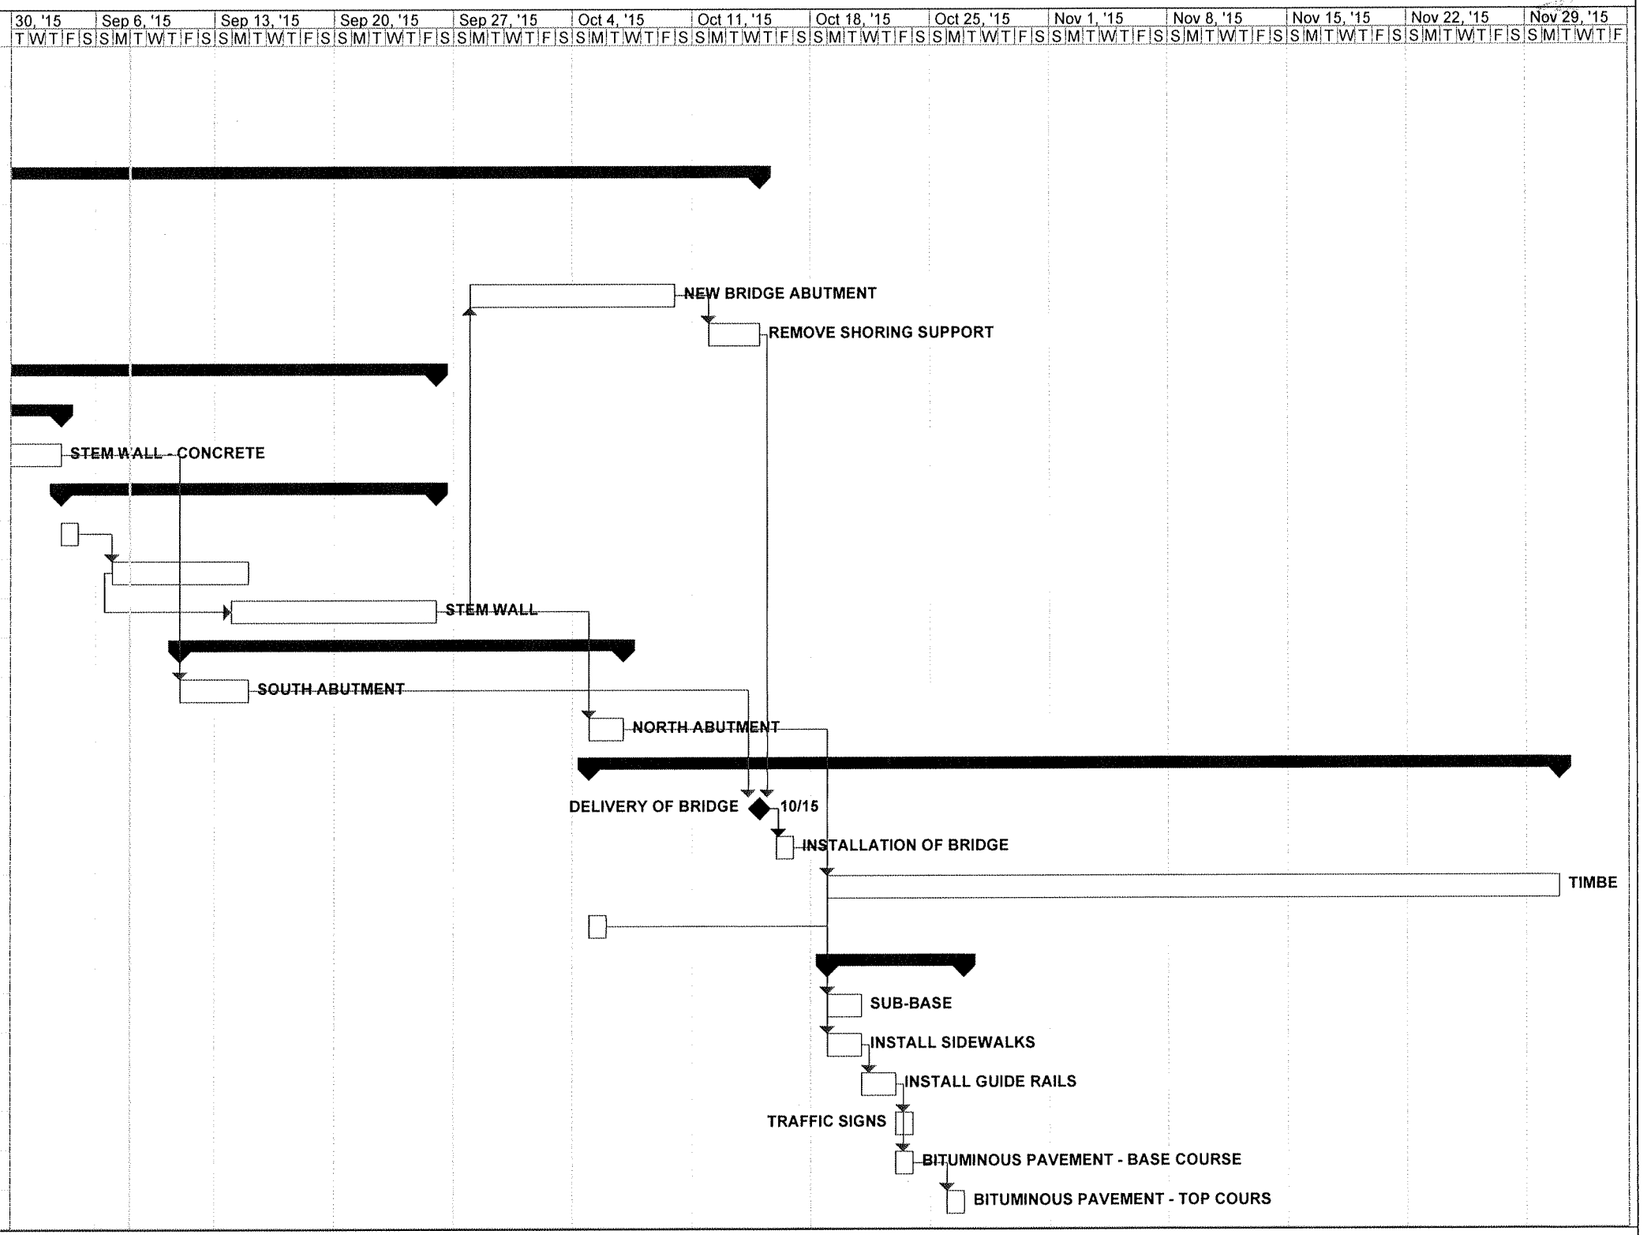


Project: Project Schedule 2015 0902
Date: Tue 9/8/15

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
